


VALENCIA LIFT STATION REHABILITATION



Newly Coated Wet Well



Crews Performing Spark Test in Wet Well

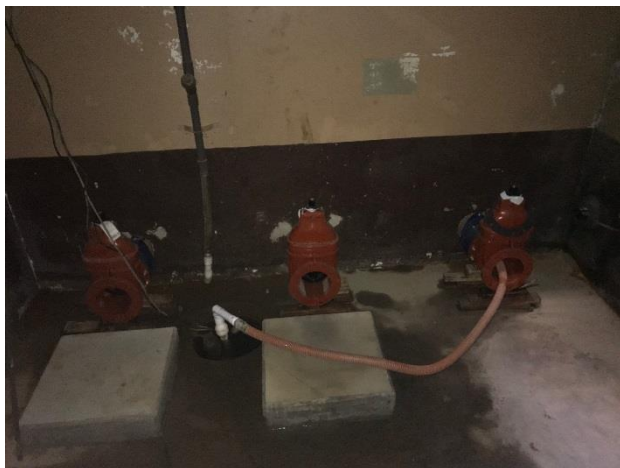

Newly Installed Valves

PROJECT LOCATION:

Laguna Hills

PROJECT SCOPE:

The project includes: the demolition of the existing pumps, mechanical piping and electrical equipment, including hazardous material abatement; rehabilitation of the wet well, including removal of the existing lining; concrete repairs and application of a new spray-on lining system; and the installation of new pumps, mechanical piping and electrical equipment.

Construction documents for this project were prepared by NV5.

PROJECT DETAILS:

- Contract Award - 03/15/2018
- Construction Contract - \$775,435
- Percentage Constructed - 45%
- Estimated Completion - August 2019

NOTES:

Demolition work and wet well coating is complete. Currently waiting on delivery of new pumps and electrical components. Pumps are scheduled to arrive June 1st.
