


FUELING STATION



Existing Fueling Station

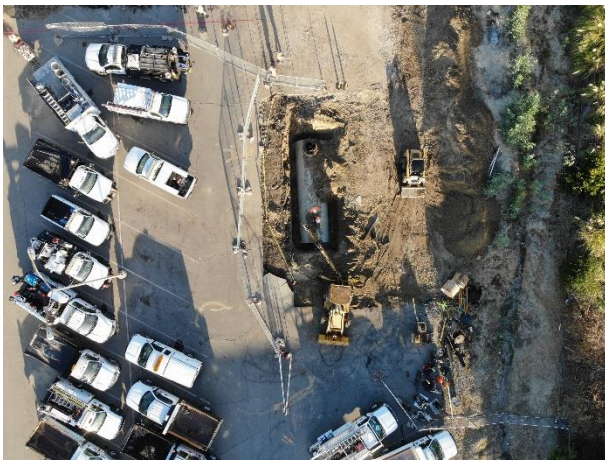

Removal of Existing Fuel Storage Tank

PROJECT LOCATION:

Laguna Hills

PROJECT SCOPE:

The proposed Fueling Station consists of the demolition and disposal of the existing underground storage tank, dispenser island, and canopy, along with the construction of a new fueling system with new underground storage tanks, a new fuel dispensing island, and all supporting power and controls for an operable facility.

Construction documents for the Fueling Station project were prepared by Ware Malcomb.

PROJECT DETAILS:

- Contract Award - 05/09/2019
- Construction Amount - \$1,388,336
- Percentage Constructed - 5%
- Estimated Completion - February 2021

NOTES:

Demolition of the existing storage tank, dispenser island, and canopy has been completed. Submittals, permitting, and procurement of new fueling system has begun.
