


VALENCIA LIFT STATION REHABILITATION



Newly Installed Pump and Motor

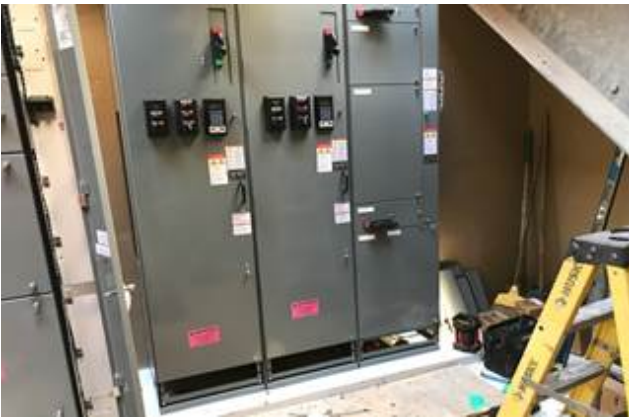

Newly Installed VFDs



Newly Installed Electrical Switchgear

PROJECT LOCATION:

Laguna Hills

PROJECT SCOPE:

The project includes: the removal of existing pumps, mechanical piping, and electrical equipment, including hazardous material abatement; rehabilitation of the wet well, including removal of the existing lining; concrete repairs and application of a new spray-on lining system; and the installation of new pumps, mechanical piping, and electrical equipment.

Construction documents for this project were prepared by NV5.

PROJECT DETAILS:

- Contract Award - 03/15/2018
- Construction Amount - \$811,528
- Percentage Constructed - 95%
- Estimated Completion - August 2020

NOTES:

Electrical component installation, startup and testing, and punch list items remain.
