


CABOT CIP FLOW CONTROL VALVE NO.1 UPGRADE

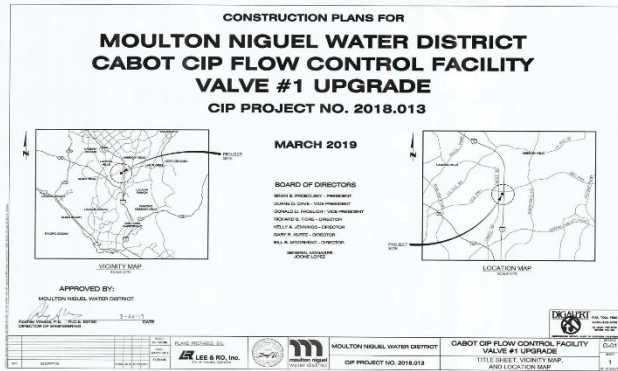

PROJECT LOCATION:

Laguna Hills

PROJECT SCOPE:

The Cabot CIP Flow Control Valve No. 1 Upgrade project will replace the existing 8-inch flow control valve, pressure reducing and sustaining valve, flow meter, isolation valves, and associated piping with new 12-inch facilities.

Construction documents were prepared by Lee & Ro, Inc.

Cabot CIP Flow Control Valve Upgrade



PROJECT DETAILS:

- Contract Award - 05/09/2019
- Construction Amount - \$225,425
- Percentage Constructed - 0%
- Estimated Completion - September 2020

NOTES:

Construction is anticipated to begin in August.

Cabot Flow Control Facility Site Overview



Existing Valves and Piping to be Replaced
