


SADDLEBACK AUXILIARY PUMP AND ENGINE REPLACEMENT, AND PORTABLE GENERATOR CONNECTION

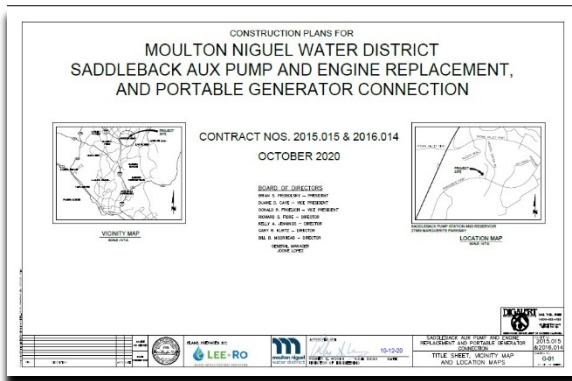

PROJECT LOCATION:

Various Locations

PROJECT SCOPE:

Work for this project will replace the existing auxiliary pump and engine with a new diesel engine-driven vertical turbine pump. The project also includes associated fuel piping, fuel storage tanks, ventilation, electrical, controls, appurtenances, portable generator connection, and building modifications.

Construction documents for the project were prepared by Lee & Ro, Inc.

PROJECT DETAILS:

- Contract Award - 10/12/2020
- Construction Contract - \$1,069,895
- Percentage Constructed - 0%
- Estimated Completion - June 2022

NOTES:

Submittals are complete. Procurement of materials is underway. Work anticipated to begin in early October.



Existing Fuel Storage to be Replaced



Existing Piping to be Replaced
