



EASTERN TRANSMISSION MAIN ACCESS MANWAYS AND VALVES



Newly Built Manway Access Point

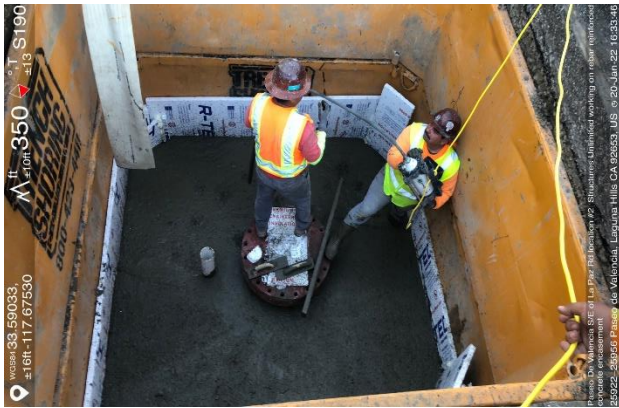

Reinforced Concrete Encasement at Paseo De Valencia Location

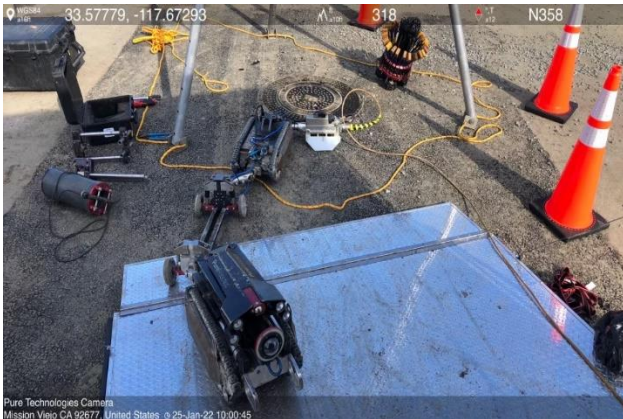

Pure Shot Robotics Camera Prior Inspection

PROJECT LOCATION:

Various Locations.

PROJECT SCOPE:

Work for this project includes installation of five new access manways along the pipeline as well as potholing, traffic control and other support required to facilitate the condition assessment, replacement of an existing in-line valve and installation of a blow-off assembly that will help with draining the pipeline prior to the condition assessment.

Construction documents for the project were prepared by Black & Veatch.

PROJECT DETAILS:

- Contract Award – 09/10/2021
- Construction Contract - \$852,102
- Percentage Constructed - 80%
- Estimated Completion - March 2022

NOTES:

Initial manway construction is complete. Robot inspection began last week of January.
