


CAMINO CAPISTRANO YARD IMPROVEMENTS



Relocation of Existing Power Lines and Poles

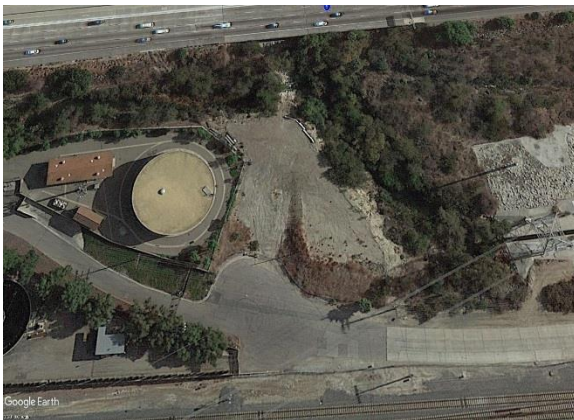

Project Location



Existing Camino Capistrano Yard Conditions

PROJECT LOCATION:

Mission Viejo

PROJECT SCOPE:

Providing a secondary operations yard utilized for material bins, pipe storage and spoils material to accommodate the Districts current needs.

The proposed work for this project includes grading; concrete material bin construction; paving; drainage improvements; fencing; lighting; and construction of a decanting and storage system for excavated wet soils.

Construction documents for the Camino Capistrano Operations Yard Improvements project were prepared by Tetra Tech.

PROJECT DETAILS:

- Contract Award - 09/20/2018
- Construction Contract - \$1,397,727
- Percentage Constructed - 5%
- Est. Completion - June 2019

NOTES:

Construction began mid-January with relocation of existing power lines and poles. Site improvement work to begin mid-February.
