


54-INCH CENTRAL INTERTIE PIPELINE IMPROVEMENTS PROJECT



54-Inch Central Intertie Improvement Project

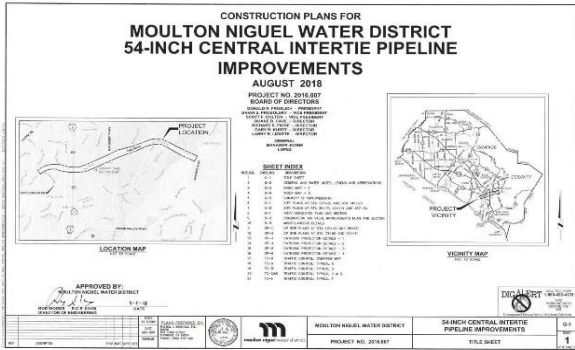

Typical Required Manway Entry



Existing Air Vent to be Replaced

PROJECT LOCATION:

Mission Viejo

PROJECT SCOPE:

This project is a result of the improvement recommendations from our recent condition assessments of the Central Intertie Pipeline.

Work includes: installing an impressed current cathodic protection system; replacing corroded appurtenances; lining corroded vault vent piping; relocating and replacing air-release valves; and sealing manway vaults from water intrusion.

Construction documents for the project were prepared by Dudek and V&A Consulting.

PROJECT DETAILS:

- Contract Award - 10/18/2018
- Construction Contract - \$1,864,400
- Percentage Constructed - 5%
- Estimated Completion - July 2019

NOTES:

Construction commenced on May 6th.
