


54-INCH CENTRAL INTERTIE PIPELINE IMPROVEMENTS PROJECT



New Rectifier at Bridlewood Flow Control Facility



Installation of New Air Vac on Oso Parkway

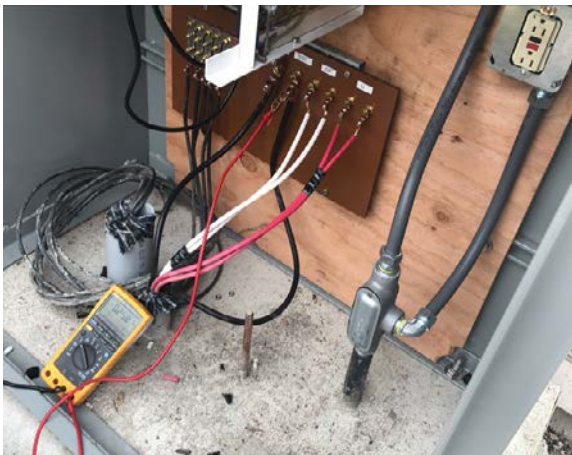

Testing of New Rectifier

PROJECT LOCATION:

Mission Viejo

PROJECT SCOPE:

This project is a result of the improvement recommendations from the condition assessment of the Central Intertie Pipeline.

Work includes installing an impressed current cathodic protection system; replacing appurtenances; lining vault vent piping; relocating and replacing air-release valves; and sealing manway vaults from water intrusion.

Construction documents for the project were prepared by Dudek and V&A Consulting.

PROJECT DETAILS:

- Contract Award - 10/18/2018
- Construction Amount - \$1,980,465
- Percentage Constructed - 95%
- Estimated Completion - June 2020

NOTES:

Electrical work and startup of cathodic protection system to be completed in early June.
