


54-INCH CENTRAL INTERTIE PIPELINE IMPROVEMENTS PROJECT



54-Inch Central Intertie Improvement Project

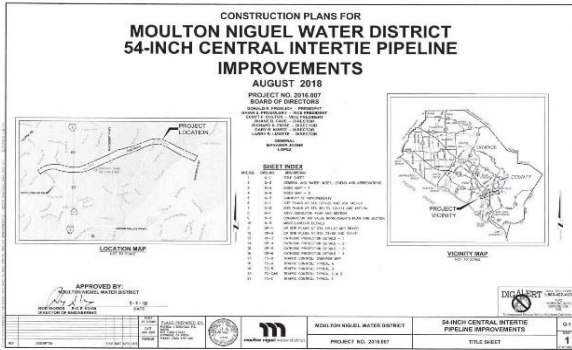

Typical Required Manway Entry



Existing Air Vent to be Replaced

PROJECT LOCATION:

Mission Viejo

PROJECT SCOPE:

This project is a result of the improvement recommendations from our condition assessment of the Central Intertie Pipeline. MFL (Magnetic Flux Leakage) inspection was utilized for the detection and verification of repairs that will be needed.

Work includes installing an impressed current cathodic protection system; replacing corroded appurtenances; lining corroded vault vent piping; relocating and replacing air-release valves; and sealing manway vaults from water intrusion.

Construction documents for the project were prepared by Dudek and V&A Consulting.

PROJECT DETAILS:

- Contract Award - 10/18/2018
- Construction Contract - \$1,864,400
- Percentage Constructed - 0%
- Estimated Completion - June 2019

NOTES:

Currently reviewing submittals. Construction is anticipated to begin in March.
